Local Plan Timetable: Local Plan 2025-2040

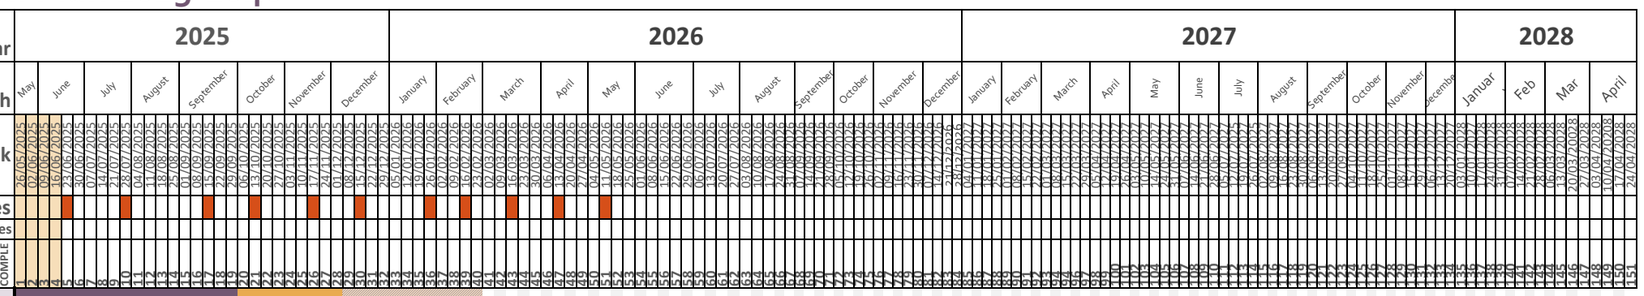

Periods	ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLE
Evidence Gathering	1. Conservation Area Appraisal	1	19	1	40	70%
	1a Heritage Led-Design Codes (PSDF YR2)	20	4			0%
	2. Housing and Economic Needs Assessment	11	12			0%
	3. Strategic Flood Risk Assessment	24	4			0%
	4. Renewable Energy Capacity Study	28	4			0%
	5. Recreational Pressure Assessment	31	4			0%
	7. Climate change/flood Risk	35	4			0%
	6. SEIA/HRA/EqIA	10	134			0%
Decision Point - if New Regime is taken progress through Gateways						
Planning Authorities give notice of start of plan-making	**Notify Pins**	10	1			
Planning Authorities give notice of start of plan-making / 4 Months Notice / Scoping and Early Participation	**Project Initiation Document (PID)**	11	2			0%
	Preparation of Plan Timetable	12	2			0%
	Monitoring Requirements	14	16			0%
Gateway 1 (Advisory)	**Notify PINS**	30	98			
Start of 30 month Local Plan Period / 23 Months / Plan Visioning and strategy develoment	**Undertake Visioning about the future of the area and confirming evidence requirements**	28	10			0%
	Public Consultation	38	8			
	Identifying and Testing spatial options and local priorities from the public consultation	46	8			0%
Gateway 2 (Advisory)	**Notify PINS**	54	1			
23 Months / Evidence Gathering and drafting the plan	**Production of proportionate evidence to demonstrate soundness of the plan**	10	119			0%
	continous engagement with members to ensure sign off	10	119			0%
Engagement, proposing changes, submission	**Communities, statutory bodies and other stakeholders able to comment on the draft plan.**	54	6			0%
	Opportunity to make changes before formal submission	60	3			0%

Gateway 3 (Stop/Go)

		Periods	ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLE
Gateway 3 (Stop/Go)	6 months	Examination	**Examination in public by an examiner appointed by Secretary of State to check that the plan is sound and legally compliant**					0%
			Those making representations will have					0%
								0%
	1 month	Finalisation and adoption of digital plan	**Monitoring**					0%

Year: 2025, 2026, 2027, 2028

Month: May, June, July, August, September, October, November, December, January, February, March, April, May, June, July, August, September, October, November, December, January, February, March, April, May, June, July, August, September, October, November, December, Januar, Feb, Mar, April

Day/Week: 26/05/2025, 02/06/2025, 09/06/2025, 16/06/2025, 23/06/2025, 30/06/2025, 07/07/2025, 14/07/2025, 21/07/2025, 28/07/2025, 04/08/2025, 11/08/2025, 18/08/2025, 25/08/2025, 01/09/2025, 08/09/2025, 15/09/2025, 22/09/2025, 29/09/2025, 06/10/2025, 13/10/2025, 20/10/2025, 27/10/2025, 03/11/2025, 10/11/2025, 17/11/2025, 24/11/2025, 01/12/2025, 08/12/2025, 15/12/2025, 22/12/2025, 29/12/2025, 05/01/2026, 12/01/2026, 19/01/2026, 26/01/2026, 02/02/2026, 09/02/2026, 16/02/2026, 23/02/2026, 02/03/2026, 09/03/2026, 16/03/2026, 23/03/2026, 30/03/2026, 06/04/2026, 13/04/2026, 20/04/2026, 27/04/2026, 04/05/2026, 11/05/2026, 18/05/2026, 25/05/2026, 01/06/2026, 08/06/2026, 15/06/2026, 22/06/2026, 29/06/2026, 06/07/2026, 13/07/2026, 20/07/2026, 27/07/2026, 03/08/2026, 10/08/2026, 17/08/2026, 24/08/2026, 31/08/2026, 07/09/2026, 14/09/2026, 21/09/2026, 28/09/2026, 05/10/2026, 12/10/2026, 19/10/2026, 26/10/2026, 02/11/2026, 09/11/2026, 16/11/2026, 23/11/2026, 30/11/2026, 07/12/2026, 14/12/2026, 21/12/2026, 28/12/2026, 04/01/2027, 11/01/2027, 18/01/2027, 25/01/2027, 01/02/2027, 08/02/2027, 15/02/2027, 22/02/2027, 01/03/2027, 08/03/2027, 15/03/2027, 22/03/2027, 29/03/2027, 05/04/2027, 12/04/2027, 19/04/2027, 26/04/2027, 03/05/2027, 10/05/2027, 17/05/2027, 24/05/2027, 31/05/2027, 07/06/2027, 14/06/2027, 21/06/2027, 28/06/2027, 05/07/2027, 12/07/2027, 19/07/2027, 26/07/2027, 02/08/2027, 09/08/2027, 16/08/2027, 23/08/2027, 30/08/2027, 06/09/2027, 13/09/2027, 20/09/2027, 27/09/2027, 04/10/2027, 11/10/2027, 18/10/2027, 25/10/2027, 01/11/2027, 08/11/2027, 15/11/2027, 22/11/2027, 29/11/2027, 06/12/2027, 13/12/2027, 20/12/2027, 27/12/2027, 03/01/2028, 10/01/2028, 17/01/2028, 24/01/2028, 31/01/2028, 07/02/2028, 14/02/2028, 21/02/2028, 28/02/2028, 06/03/2028, 13/03/2028, 20/03/2028, 27/03/2028, 03/04/2028, 10/04/2028, 17/04/2028, 24/04/2028

Full Council Dates

Steering Group Meeting Dates

Select a period to highlight at right. A legend describing the chart Period 1 | Plan Duration | Actual Start | % Complete | Actual (beyond plan) | % Complete (beyond plan)
